THE ANNOUNCEMENT ROOM
What happened. Why it matters. What comes next.

ASX: FRS | FORRESTANIA RESOURCES LIMITED 16 October 2026 | OPERATIONAL UPDATE

Forrestania targets mid-December first ore at Edna May

Forrestania says the Edna May gold plant could process its first ore in mid-December 2026, subject to final equipment arriving and being installed. The plant was acquired from Ramelius Resources in September. Lake Johnston, its second plant, is now described as starting in early 2027.

Mid-Dec

Edna May first ore target

2026. Subject to final equipment components

Late Nov

Mill liners due on site


First tailings storage cell also due late November

Early 2027

Lake Johnston start

Commissioning and production. Earlier papers said late 2026

HOW THE COMPANY'S TIMING HAS BEEN WORDED (BARS SHOW WORDING, NOT EXACT DATES)

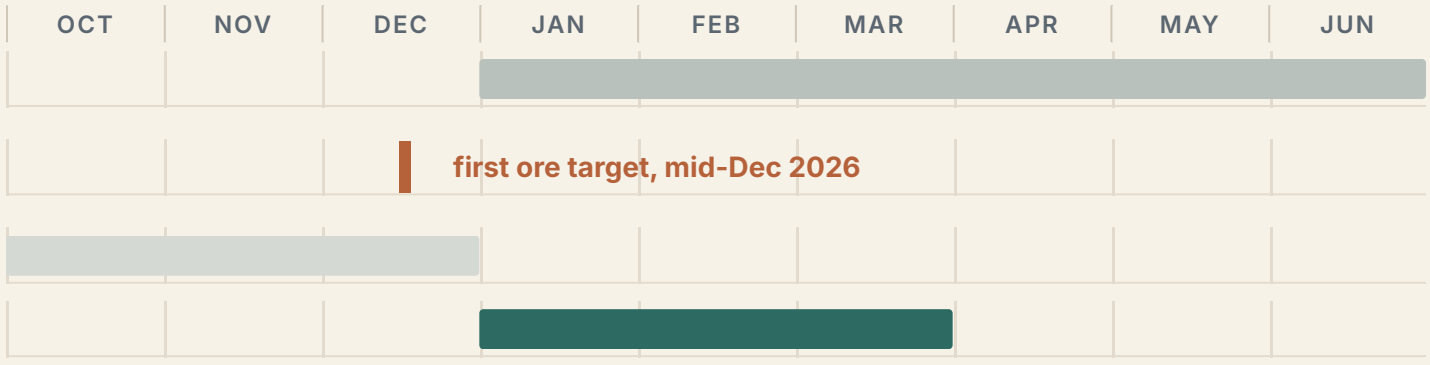

Grey bars are earlier statements. Orange and teal are the 16 Oct statements. First ore is a different milestone from the June mill-restart target, and the company has not restated a full restart date. It has not said whether Lake Johnston has been delayed. Quarters shown are TAR's rough reading of "late 2026" and "early 2027".

WHAT THE 16 OCTOBER RELEASE REPORTS

- **Edna May liners:** mill liner shipment is underway, due on site in the final week of November.
- **Edna May tailings:** first cell of the tailings storage facility (TSF) is progressing toward completion in late November.
- **Edna May plant:** final critical-path maintenance and refurbishment is progressing.
- **Lake Johnston elution circuit:** hot commissioning is underway. This is at Lake Johnston, not Edna May.
- **Lake Johnston plant:** refurbishment and procurement continue ahead of commissioning and production in early 2027.
- **Mining:** contractor equipment is mobilising to Tycho and Johnson Range. The release does not say which deposit supplies the first ore.

WHAT THE RELEASE DOES NOT SAY

It gives no tonnes, grade, cost or gold output for the ore to be processed from mid-December, and no cash, funding or capital figures. Photo captions show first ore delivery and dozer work at the Edna May run-of-mine pad, but the text does not say how much ore or from which deposit. First ore is a target, not a result.

WHAT FRS DOES Forrestania is building a Western Australian gold business around two processing plants, Edna May and Lake Johnston. Its company profile names Tycho, Johnson Range and surrounding projects as Edna May ore sources.

Sources: FRS ASX releases: operational update (16 Oct 2026), Edna May acquisition (29 Jun 2026), completion (4 Sep 2026), tailings contract (14 Sep 2026); 2026 Annual Report (14 Sep 2026). Company statements and targets, unaudited. Market data is not included.

First ore and full restart are separate milestones

EDNA MAY STUDY: PRE-TAX FREE CASH FLOW (A$ MILLION)



Two sensitivity cases from the 18 Sep study, not a trend. Bars start at zero.

A$3,293/oz

AVERAGE AISC IN THE STUDY AT A$5,500/OZ

AISC is all-in sustaining cost per ounce. It was A$3,313/oz at the higher gold price. The study covers a 402.8koz Ore Reserve, about 374.6koz of gold, over 10 years of mining.

READ THE STUDY FIGURES WITH THEIR LIMITS

Free cash flow is pre-tax and undiscounted, and no NPV was published. Modelled start is January 2030, and the Stage 3 pit cutback behind it is not yet approved. The A$98.0m project capital excludes plant refurbishment. Capital accuracy is plus or minus 30%. These are company estimates, not reported results.

THREE DEVELOPMENTS INVESTORS SHOULD UNDERSTAND

01 The first ore is not the study ore — REPORTED

The study economics belong to the Edna May Ore Reserve, modelled from January 2030. The release does not say which deposit supplies the December ore, so Tycho and Johnson Range cannot be assumed to be the source. With no grade, tonnes or cost given, the study figures cannot be applied to it.

02 The date depends on equipment and tailings — TARGET | CONDITIONAL

First ore is subject to the timely receipt and installation of final equipment. The 14 Sep contract release had the first TSF section operating from mid-November. The 16 Oct release says the first cell is due in late November. The company has not said whether these are the same milestone.

03 Two plants to bring online — REPORTED

Edna May cost A$300m: A$210m cash and 225 million shares valued at A$90m, completed on 4 Sep. In June the company targeted an Edna May mill restart in 1H 2027 and Lake Johnston in late 2026. Today's release targets first ore at Edna May in mid-December 2026 and Lake Johnston production in early 2027.

WHAT MANAGEMENT EXPECTS (NOT RESULTS)

- First ore mid-Dec 2026
- Liners on site late Nov
- First TSF cell late Nov
- Lake Johnston early 2027

These are management targets. The release gives no production, cost or cash figures.

WHAT TO WATCH

Liners and installation. Do the mill liners arrive and get fitted on time?

First ore and first gold. Is ore processed in mid-December, and does gold follow?

Ore detail. Which deposit feeds first ore, and at what tonnes and grade?

Approvals and Lake Johnston. Does Stage 3 get approved, and when does Lake Johnston start?

TAR TAKE

Forrestania now targets first ore at Edna May in mid-December 2026, earlier than the first-half 2027 mill restart it flagged in June, and parts are moving. But first ore is a different milestone from a full restart, which has no restated date, the date is conditional, the ore has no disclosed source, grade or cost, and the study's A$728.7m assumes a 2030 start and a pit cutback that is not yet approved. The next tests are liner delivery, first ore in December, a full restart date and the Lake Johnston start.

Sources: FRS ASX releases: operational update (16 Oct 2026), Edna May pre-feasibility study and Ore Reserve (18 Sep 2026), tailings contract (14 Sep 2026), completion (4 Sep 2026), acquisition (29 Jun 2026). Study figures are company estimates and were checked against the study's cost and capital tables. Expectations are not guarantees.
